

## **QUALITY ASSURANCE**







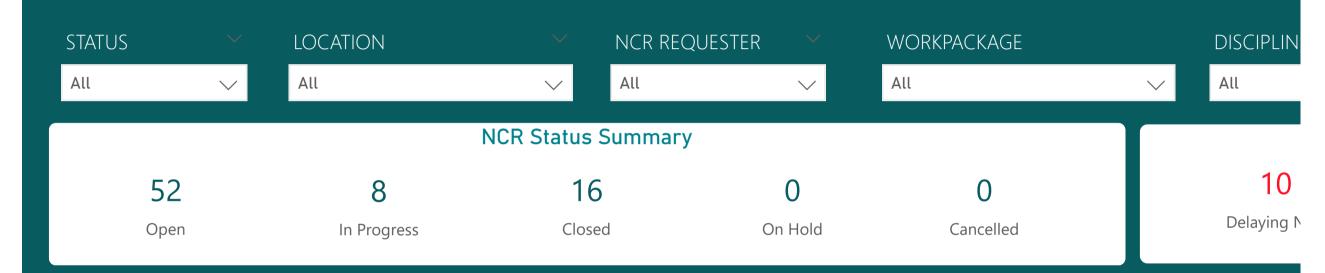

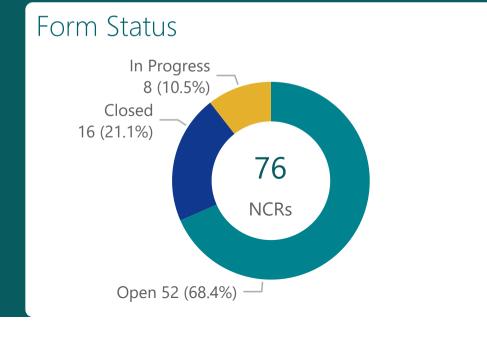

#### **QUALITY ASSURANCE**


#### Non-Conformance Report Monitoring Dashboard













#### LATEST NCR's STATUS & DETAILS NCR No. Created Date Last Modified Latest Title/Subject of the NCR Severity Category Corrective Action -NCR T Latest Corrective Action -Progress (Sch1) Target Date Implementation Date Status Date 27 Feb 2024 03 Jul 2024 NCR 22 Open 2 South Shaft - IFC Drawings Inacurate Pile Coordinates Major NC Tuesday, June 25, **Process** 2024 03 Jul 2024 In Progress 5 Minor NC NCR 28 12 Mar 2024 Diameter of secant piles in rock layer Product 2024-04-26 NCR 34 11 Apr 2024 03 Jul 2024 Open 2 2024-NCR-1-SENER - Design Quality Audit Finding (KPI's) Thursday, June 27, Minor NC **Process** 2024 NCR 35 11 Apr 2024 03 Jul 2024 2024-NCR-2-SENER - Design Quality Audit (documented Minor NC Friday, June 28, Open 2 **Process** information lack of traceability) 2024 03 May 2024 03 Jul 2024 Major NC NCR 49 Open Improper Concrete Consolidation - Noise Wall Concrete Product Foundation NCR 77 03 Jul 2024 03 Jul 2024 Open Missed concrete test on a filler pile F12 Minor NC **Process**

## Non-Conformance Report Monitoring Dashboard









27
Issued from FC

16 Closed from FC


**1**Open During This Month


8
In Progress During This Month

1 Closed During This Month Report Month

Multiple selections

Related NCR No.	Description	Actual Implementation Date	Action Imple
NCR2	To prevent a recurrence will modify the language within all contracts stating: "No Work Shall Proceed without the Written Authorization from the Safety Department and the Site Manager." will develop a process which ensures subcontractors work plans and personnel are approved to proceed with work.	Monday, May 15, 2023	The root cau the contract the schedule with this wo
NCR5	Improved communications are necessary between the Construction and Quality Teams.  In order to prevent recurrence, the following has been / will be implemented: - Issuance of a weekly 3-weeks look-ahead by each Construction Manager, used by the Construction Quality  Department to prepare the ITP Two-Week Look-Ahead, as requested in PA -  (vi) - Issuance of the ITP Two-Week Look-Ahead at the beginning of each week to the CA representatives, by e-mail - Use of the ITP Two-Week Look-Ahead as the Witness & Hold Points advance written notice, as requested in PA Issuance of written amendments as a follow-up to the ITP Two-Week Look-Ahead e-mail	Friday, July 21, 2023	This non-cor the Construct Boreholes at Root cause:
NCR8	The subcontractor was requested to provide mitigation measures to prevent a re-occurrences.  The sediment deposition has been cleaned from the sidewalk and the road.  Filter fabric has been replaced for the two catch basins.	Friday, July 21, 2023	Exhibition - near the surl make its way in place in a and/or funct
Total			

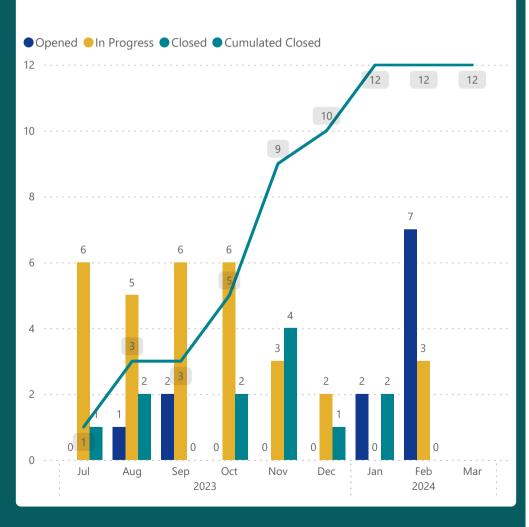









# Current Step Disposition

#### Pending Action Summary

Negative value (in red) indicates a delay

NCR No.	Latest Status	Target Day	Days Left	Current Target Action	Subject of NCR
NCR 39	Open	08 May 2024	41	Disposition & CAR Planning	Vibration limit exc
NCR 49	Open	24 May 2024	29	Disposition & CAR Planning	Improper Concret
NCR 51	Open	28 May 2024	27	Disposition & CAR Planning	UTI - AES - No co base of the paving
NCR 52	Open	28 May 2024	27	Disposition & CAR Planning	Concrete Placeme
NCR 59	Open	25 Jun 2024	7	Disposition & CAR Planning	Pre-Testing of Tre
NCR 62	Open	02 Jul 2024	2	Disposition & CAR Planning	Concrete Poured
NCR 63	Open	03 Jul 2024	1	Disposition & CAR Planning	2024-NCR-1-AEC
NCR 64	Open	03 Jul 2024	1	Disposition & CAR Planning	2024-NCR-2-AEC

16 Closed & Delayed NCRs



## Late NCR Summary

NCR No.	Latest Status	Late Type	Disposition	Remedy Action	Corrective Action
NCR 13	Closed	Corrective Action, Verification			
<u>NCR 15</u>	In Progress	Disposition & CAR Planning, Corrective Action, Verification			
NCR 16	Closed	Disposition & CAR Planning, Verification			
NCR 17	In Progress	Disposition & CAR Planning, Verification			
NCR 18	In Progress	Disposition & CAR Planning, Remedy Action			
NCR 19	Closed	Disposition & CAR Planning, Verification			
NCR 20	Closed	Disposition & CAR Planning, Verification			
NCR 21	In Progress	Disposition & CAR Planning, Corrective Action, Verification			
NCR 22	Open	Disposition & CAR Planning			
NCR 24	Open	Disposition & CAR			
