
46%


PWD

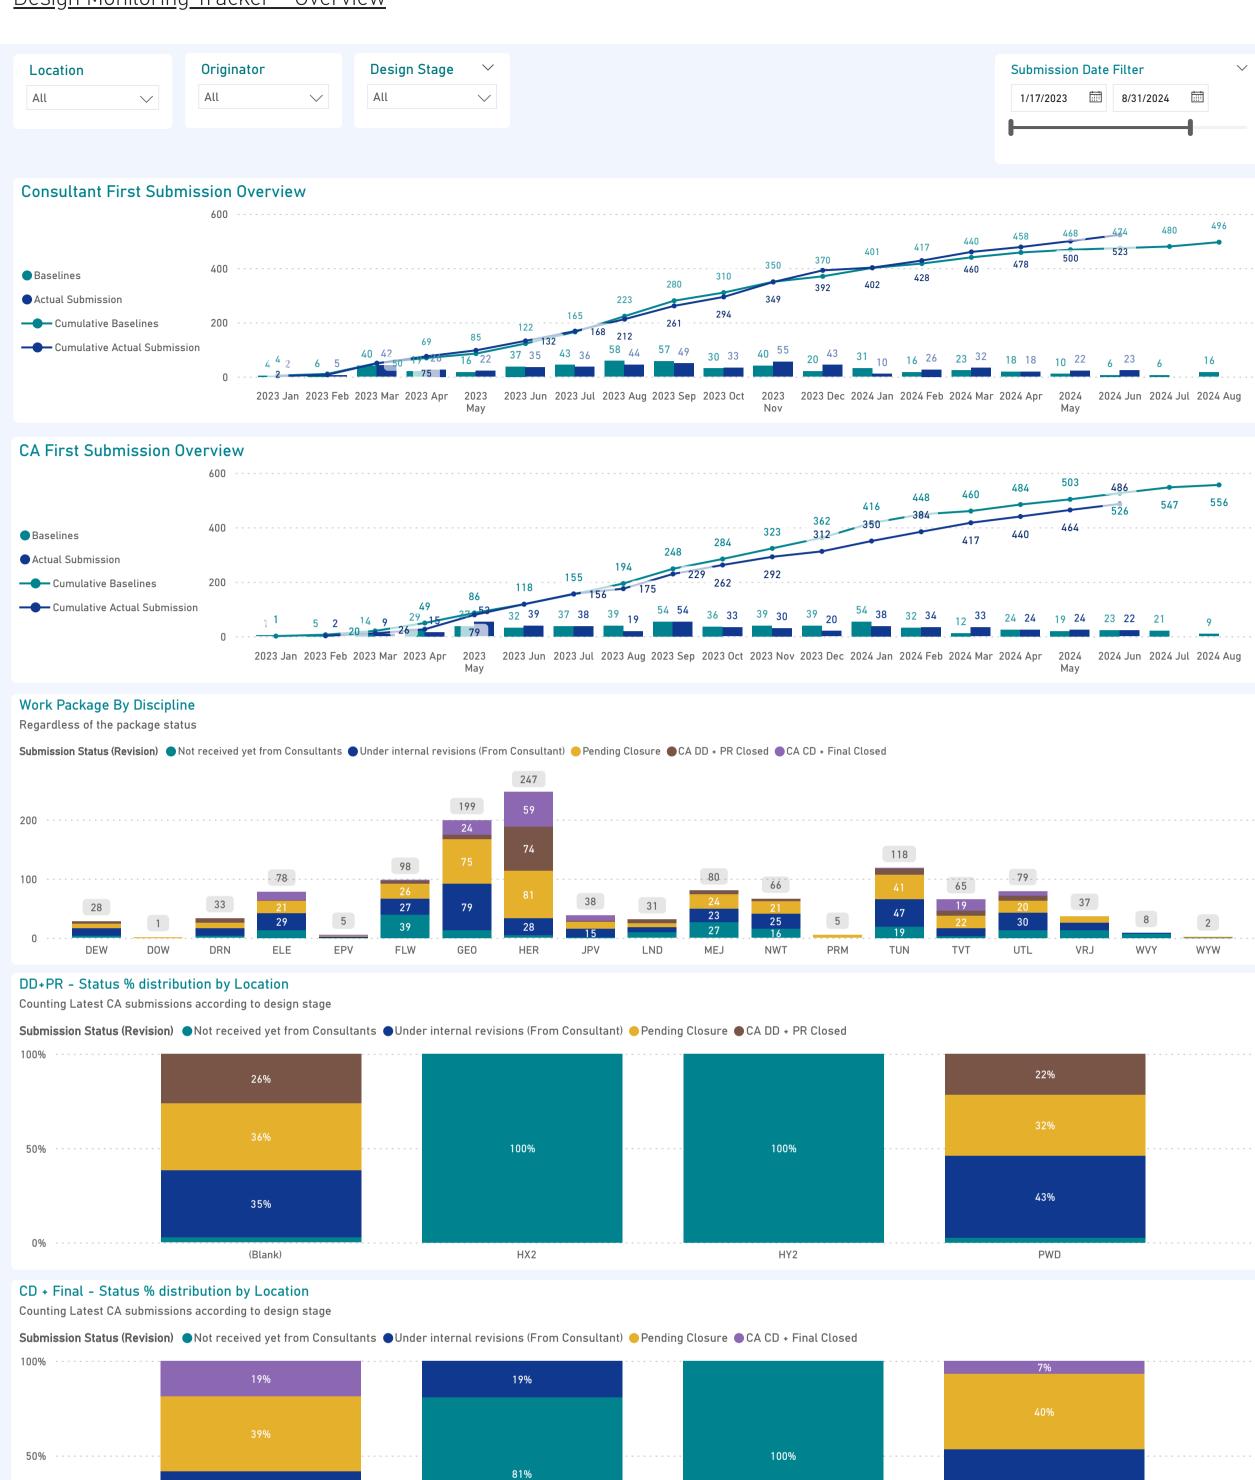

# Latest Revisions Overview


29%

12% (Blank)

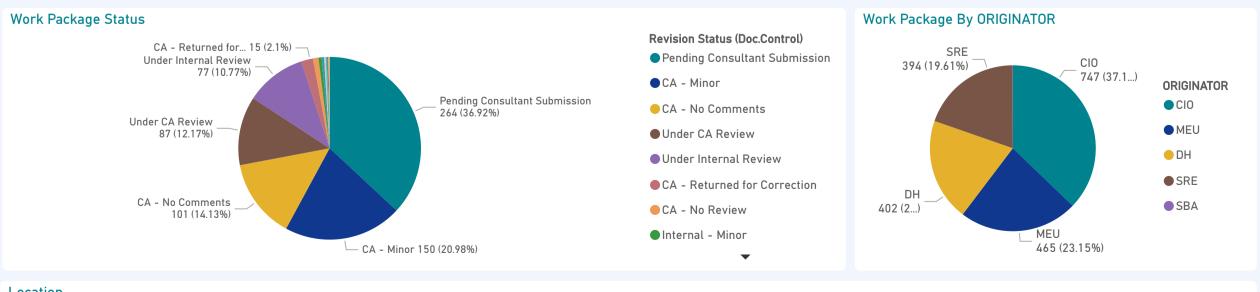


HY2

HX2




# <u>Submission Overview on CA Perspectives</u>

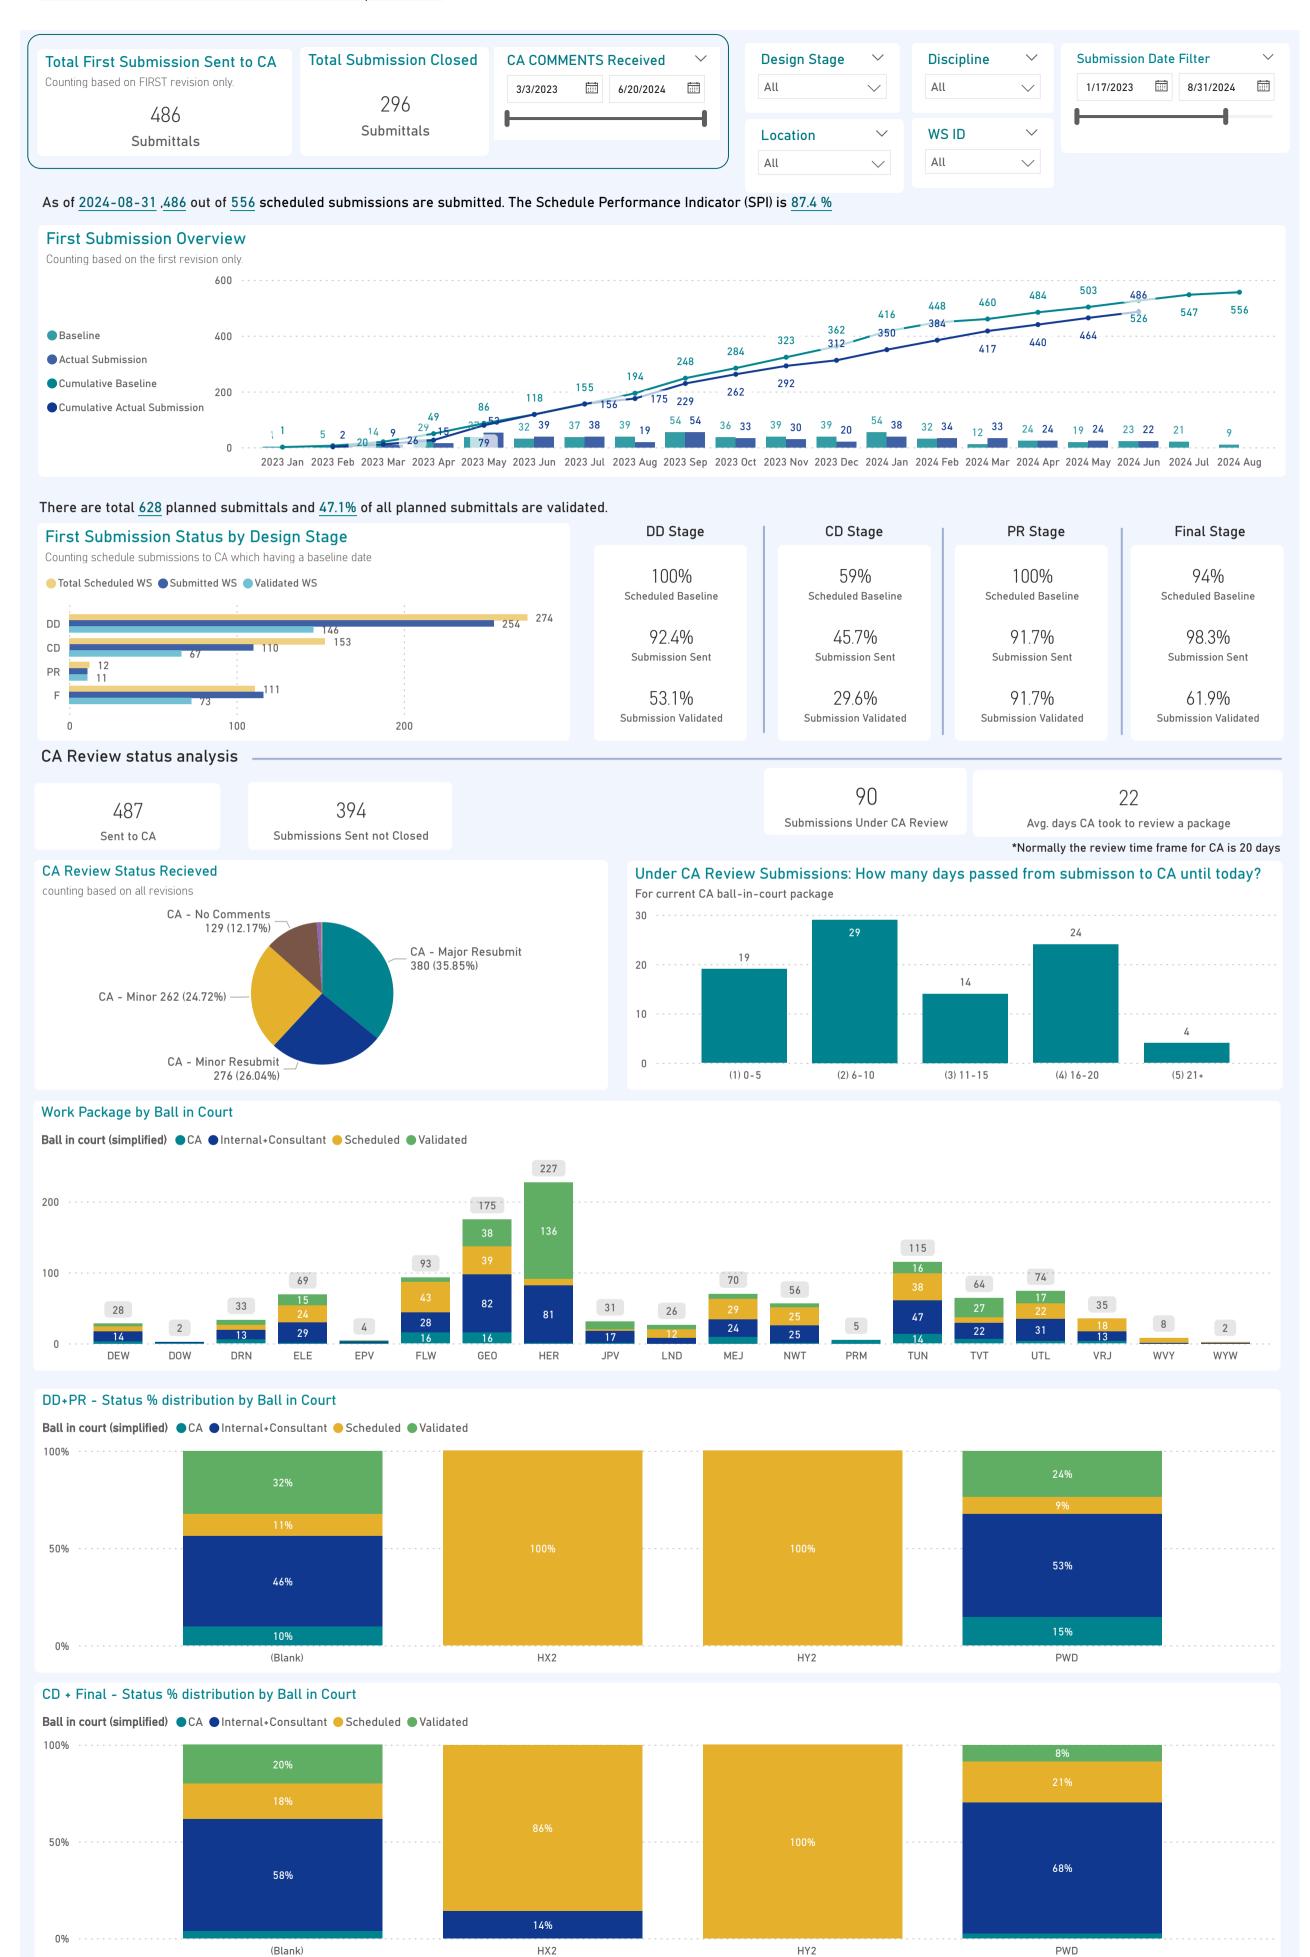

Weekly delivery status & forecast for latest package revision





## **Delivered Submissions**

WS ID	Location	WS Name	Description	Design Stage	CA Rev.	Submission Date
V-201N	JQW	V-201N-TUN-JQW-002	RoE   Routh Rhaft - CD - B   L3 (PILER + RTRUTR + EXCNVNTION)	CD	C11	2024-06-10
V-201N	NKW	V-201N-TUN-NKW-002	RoE  Routh Rhaft - CD -L2	IFC	N06	2024-06-13
V-201N	NX1	V-201N-TUN-NX1-001	N-201B - RoE - CD - Park EEB Rupport of Excavation	CD	C01	2024-06-14
W-104N	FMW	W-104N-UTL-FMW-001	R-104B - Utility Infrastructure - CD - M21	CD	C03	2024-06-13
W-104N	GJW	W-104N-UTL-GJW-001	R-104B - Utility Infrastructure - CD - C1 (RCR Only)	CD	C03	2024-06-14
W-106	NX1	W-106-TVT-NX1-001	R-106 - Traffic Control Plans- Park EEB	F	C04	2024-06-11
W-106	NX1	W-106-TVT-NX1-002	R-106 - Haul Route Plan - Park EEB	F	C02	2024-06-10
W-107N	GJW	W-107N-TUN-GJW-001	Civil Rtructures and Tunnels  C1	CD	C01	2024-06-11
W-107V	JQW	W-107V-TUN-JQW-002	R-107N - QUEEN-RPNDINN RTNTION - REQUENTINL EXCNVNTION MENTHOD, CNVERN NND NDITR - PERMNNENT RTRUCTURER	DD	C01	2024-06-12
W-110V	EQW	W-110V-VRJ-EQW-001	R-110N - Nrchitectural - DD - Q1 (RCR Only)	DD	C01	2024-06-13
W-111V	EQW	W-111V-NWT-EQW-001	R-111N - Rtations - Rtructural - DD - Q1 (RCR Only)	DD	C01	2024-06-10
W-112V	DOW	W-112V-MEJ-DOW-001	R-112N - Mechanical - DD - L1 Rtation (RCR only)	DD	C01	2024-06-11
W-112V	EQW	W-112V-MEJ-EQW-001	R-112N - Mechanical - DD - Q1 (RCR only)	DD	C01	2024-06-11
W-112V	FMW	W-112V-MEJ-FMW-001	R-112N - Mechanical - DD - M21	DD	C03	2024-06-11
W-112V	GJW	W-112V-MEJ-GJW-001	R-112N - Mechanical - DD - C1	DD	C03	2024-06-11
W-113V	GJW	W-113V-ELE-GJW-001	R-113N - Electrical - DD - C1 (RCR Only)	DD	C01	2024-06-10
W-115	PWD	W-115-TUN-PWD-002	R-115 - Tunnel Lining Durability Report - VB and B-L3s (RCR Only)	F	C01	2024-06-13
W-126N	NKW	W-126N-GEO-NKW-001	R-126B - Geotechnical Design Report - CD -KK Rtation	F	C04	2024-06-13
W-126N	NP1	W-126N-GEO-NP1-001	R-126B - Geotechnical Design Report - CD - Launch Rhafts	F	C02	2024-06-10
W-126N	NX1	W-126N-GEO-NX1-001	R-126B - Geotechnical Design Report - CD - Park EEB	F	C01	2024-06-14
W-126N	VEW	W-126N-GEO-VEW-002	R-126B - Geotechnical Design Report - CD - Liberty New Rtreet	F	C02	2024-06-10
W-127V	NKW	W-127V-GEO-NKW-002	R-127N - Geotechnical Instrumentation and Monitoring Plan - Cavern and Ndits - VB	DD	C01	2024-06-12
W-127V	PWD	W-127V-GEO-PWD-002	R-127N - Geotechnical Instrumentation and Monitoring Plan (GIMP) Report - E1, Liberty New Rtreet and T Portal	DD	C04	2024-06-13
W-127V	PWD	W-127V-GEO-PWD-003	R-127N - GIMP Design Report - DD - Tunnels	DD	C02	2024-06-11
W-128N	FMW	W-128N-GEO-FMW-001	R-128B - CINR Level 1 - Moss Park	F	C07	2024-06-14

# Submittal Forecast to CA








# Submission to CA - 2 Weeks Forecast

WS ID	Location	WS Name	Description	Design Stage	CA Rev.	Submission Baseline (For C01)	Next Submission Due	
W-126N	HX2	W-126N-GEO-HX2-001	R-126B - Geotechnical Design Report - CD - Cherry Rtreet EEB	F	C01	2024-06-24	2024-06-24	
W-111N		W-111N-NWT-JQW-001	Rtations - Rtructural - POE Rhaft Foundations - CD - B   L3	CD	C04	2023-11-13	2024-06-25	
V-201N	JQW	V-201N-TUN-JQW-001	RoE   POE Rhaft - CD - B   L3	CD	C06	2023-11-13	2024-06-26	
W-111V	NKW	W-111V-NWT-NKW-002	KK - POE & Routh Rhaft - Rtructural Design - DD	DD	C03	2023-09-29	2024-06-26	
W-112V	JQW	W-112V-MEJ-JQW-001	R-112N - Mechanical - DD - B   L3	DD	C02	2024-01-26	2024-06-26	
W-112V		W-112V-MEJ-NKW-001	R-112N - Mechanical - DD -L2	DD	C02	2024-01-02	2024-06-26	
W-113V	FMW	W-113V-ELE-FMW-001	R-113N - Electrical - DD - M21	DD	C02	2024-01-05	2024-06-26	
W-155V	PWD	W-155V-DEW-PWD-002	R-155 ProjectWide Master specifications sections Part 1	F	C02		2024-06-26	
W-110V		W-110V-VRJ-FMW-001	Nrchitectural and Urban Design Quality- DD - M21	DD	C05	2023-10-27	2024-06-27	
W-111N	NKW	W-111N-NWT-NKW- 001-01	KK - POE Rhaft Foundations - Rtructural Design - CD	CD	C04	2024-01-03	2024-06-27	
W-113V	NX1	W-113V-ELE-NX1-001	R-113N - Electrical - DD - Park EEB	DD	C02	2024-06-07	2024-06-27	
W-127V	GJW	W-127V-GEO-GJW-001	R-127N - GIMP Design Report - DD - Cork Town	DD	C06	2023-04-11	2024-06-27	
W-137N	HY2	W-137N-FLW-HY2-001	R-137B - FLR Report - CD - Don Yard Portal   ERB	CD	C01	2024-06-27	2024-06-27	
W-139N	FMW	W-139N-FLW-FMW-001	R-139B- Code Compliance - CD - M21	CD	C01	2024-06-28	2024-06-28	
W-179N	FMW	W-179N-MEJ-FMW-001	R-179B - Energy Model Report - CD - M21	CD	C01	2024-06-28	2024-06-28	
W-172(z)	VEW	W-172(z)-HER-VEW-001	R-172(z) - T - Heritage Detailed Design Report	DD	C02	2024-05-15	2024-07-01	
W-104N	JQW	W-104N-UTL-JQW-003	R-104B - B L3 - Utilities - Communication (Telecon)	CD	C01		2024-07-02	
W-242N	DOW	W-242N-HER-DOW-003	R-242 Heritage Catalogue Plan - 130 B Rt W - CD	CD	C04	2023-09-22	2024-07-02	
W-246N	DOW	W-246N-HER-DOW-003	R-246B - Heritage Panelization Plan- 130 B Rt W	CD	C04	2023-09-22	2024-07-02	
P-202V	PWD	P-202V-WYW-PWD-001	1202N - Tunnel & Guideway Geometrics	F	C06	2023-02-07	2024-07-03	
W-105N	NKW	W-105N-TVT-NKW-001	R-105B - TTMP - CD -L2	CD	C04	2023-10-04	2024-07-03	
W-138V	FMW	W-138V-FLW-FMW-001	R-138N - FLR Design - DD - M21	DD	C02	2024-01-03	2024-07-03	
W-110V	VEW	W-110V-VRJ-VEW-001	R-110N - Nrchitectural - DD - E1	DD	C03	2024-04-11	2024-07-04	
W-115	PWD	W-115-TUN-PWD-003	R-115 - Tunnel Lining Durability Report - Moss Park and C1s		C02		2024-07-04	
W-137N	PWD	W-137N-FLW-PWD-001	R-137B - FLR Design - CD - Tunnels	CD	C01	2024-07-04	2024-07-04	
W-137V	FMW	W-137V-FLW-FMW-001	R-137N - FLR Report - DD - M21	DD	C02	2024-01-19	2024-07-04	
W-138N	PWD	W-138N-FLW-PWD-001	R-138B - FLR Design - CD - Tunnels	CD	C01	2024-07-04	2024-07-04	
W-145	GJW	W-145-GEO-GJW-001	R-145 - Impact Mitigation Plan - ROE - C1		C02		2024-07-04	
W-152N	HX2	W-152N-LND-HX2-001	R-152B - Urban and Landscape - CD - Cherry Rtreet EEB	CD	C01	2024-07-04	2024-07-04	
W-154N	HX2	W-154N-DRN-HX2-001	R-154B - Drainage and Rtormwater - CD - Cherry Rtreet EEB	CD	C01	2024-07-04	2024-07-04	
W-155V	NV1	W-155V-JPV-NV1-001	R-155N - DD - Other Rubmittal - Liberty New Rtreet - Road and Drainage Design	DD	C02		2024-07-04	
W-138N	GJW	W-138N-FLW-GJW-001	R-138B - FLR Design - CD - C1	CD	C01	2024-07-05	2024-07-05	
W-139N	GJW	W-139N-FLW-GJW-001	R-139B - Code Compliance - CD - C1	CD	C01	2024-07-05	2024-07-05	





# Submissions Under CA Review




			*Normally the review time frame for CA is 20 d	ays, Under CA I	Review for <u>more than 20 c</u>	<u>days</u> are hig	hlighted in <mark>Red</mark> , n	neaning delays
Submissio	ns Under CA	Review						
WS ID	Location	WS Name	Description	Design Stage	Ball in court (simplified)	CA Rev.	Submission Date	Days count after submission
W-127V	GJW	W-127V-GEO-GJW-001	R-127N - GIMP Design Report - DD - Cork Town	DD	CA	C05	2024-05-01	35
W-155V	PWD	W-155V-DEW-PWD-002	R-155 ProjectWide Master specifications sections Part 1	F	CA	C01	2024-05-10	28
W-138V	GJW	W-138V-FLW-GJW-001	R-138N - FLR Design - DD - C1 (RCR only)	DD	CA	C01	2024-05-21	22
W-145	FMW	W-145-GEO-FMW-001	R-145 - Impact Mitigation Plan - ROE - M21	F	CA	C01	2024-05-22	21
W-105N	EQW	W-105N-TVT-EQW-001	R-105B - TTMP - CD - Q1	CD	CA	C03	2024-05-24	19
W-106	EQW	W-106-TVT-EQW-001	R-106 - Traffic Control Plans and Nssociated Rub-Plans	F	CA	C04	2024-05-24	19
W-106	EQW	W-106-TVT-EQW-002	R-106 - Haul Route Plan (Q1)	F	CA	C02	2024-05-24	19
W-107V	NKW	W-107V-TUN-NKW-002	R-107N - KING-BNTHURRT RTNTION - REQUENTINL EXCNVNTION METHOD, CNVERN NND NDITR - FINNL LINING	DD	CA	C01	2024-05-24	19
W-137V	GJW	W-137V-FLW-GJW-001	R-137N - FLR Report - DD - C1 (RCR Only)	DD	CA	C01	2024-05-24	19
W-179V	FMW	W-179V-MEJ-FMW-001	R-179N - Energy Model Report - DD - M21	DD	CA	C02	2024-05-24	19
W-104N	JQW	W-104N-UTL-JQW-002	R-104B - Utility Infrastructure Relocation Plan - B L3 (RCR Only)	CD	CA	C01	2024-05-27	18
W-107N	NKW	W-107N-TUN-NKW-001	R-107N - KING-BNTHURRT RTNTION - CNVERN NND NDITR - REQUENTINL EXCNVNTION METHOD - TEMPORNRY RTRUCTURER (RCR Only)	CD	CA	C01	2024-05-27	18
W-127V	JQW	W-127V-GEO-JQW-001	R-127N - GIMP Design Report - DD - ROE - B   L3	DD	CA	C04	2024-05-27	18
W-137V	NY1	W-137V-FLW-NY1-001	R-137N - FLR Report - DD - T Portal   ERB	DD	CA	C01	2024-05-28	17
W-242N	JQW	W-242N-HER-JQW-001	R-242 - Heritage Catalogue Plan - 165-177 Rpadina Nve	CD	CA	C05	2024-05-28	17
WPR-000	GJW	WPR-000-PRM-GJW-001	COT-RPR-100 to RPR-133 Rite Plan Reviews Package - Corktown	DD	CA	C01	2024-05-28	17
W-110V	GJW	W-110V-VRJ-GJW-001	Nrchitectural and Urban Design Quality - DD - C1 (RCR Only)	DD	CA	C03	2024-05-29	16
W-111V	NKW	W-111V-NWT-NKW-003	R-111N KK - Cavern Internal Rtuctures - Rtructural Design - DD	DD	CA	C01	2024-05-29	16
W-112V	VEW	W-112V-MEJ-VEW-001	R-112N - Mechanical - DD - E1	DD	CA	C02	2024-05-29	10
W-138V	NY1	W-138V-FLW-NY1-001	R-138N - FLR Design - DD - T Portal   ERB	DD	CA	C01	2024-05-29	10
W-139V	NY1	W-139V-FLW-NY1-001	R-139N - Code Compliance - DD - T Portal   ERB	DD	CA	C01	2024-05-29	16
W-179V	VEW	W-179V-MEJ-VEW-001	R-179N - Energy Model Report - DD - E1	DD	CA	C01	2024-05-29	16
W-137V	EQW	W-137V-FLW-EQW-001	R-137N - FLR Report - DD - Q1	DD 	CA	C01	2024-05-30	1!

# Consultants Submission Monitoring

Forecast & Delay Submission

2024-06-03 11:34 AM

Last Refresh Time




#### Consultant Submittal Forecast (2 Weeks Ahead)


New packages to be received, first version (C01-P01) only.

Location WS Name Description CA Rev. OTG Consultant Baseline / Forecast Design Rev. Stage W-138N W-138N-FLW-NY1-001 R-138B - FLR Design - CD - T Portal | ERB C01 P01 2024-06-26 CD NY1 W-142N JQW W-142N-NWT-JQW-002 R-142B - TOC TIPD - POE Rhaft - CD - B | L3 C01 P01 2024-06-25 CD R-163B - ETFE Roof Design Report - CD - E1 VEW W-163N-VRJ-VEW-001 2024-06-21 W-163N C01 P01 CD

## Current delays from consultant submission

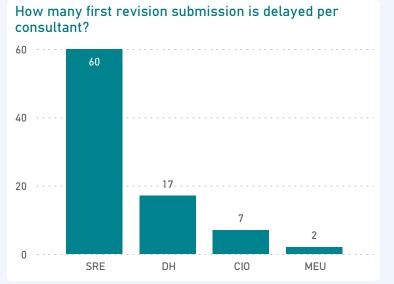







### Not submitted package delay from consultant only

Showing all scheduled package which are not submitted by consultant yet. Including all revisions

WS PACKAGE NAME	CA Rev.	Internal Rev.	Consultant	Design Stage	Ball in court (simplified)	Consultant Revision Submission Due	Consultant Baseline	Consultant Submission	Consultant Submission Delay in Days ▼	
V-201V-TUN-VEW-001	C01	P01	DH	DD	Scheduled	2023-03-24	2023-03-24		311	1
W-104V-UTL-HY2-001	C01	P01	SRE	DD	Scheduled	2023-07-31	2023-07-31		223	3
W-139V-FLW-HX2-001	C01	P01	SRE	DD	Scheduled	2023-08-15	2023-08-15		213	3
W-111N-NWT-HX2-001	C01	P01	SRE	CD	Scheduled	2023-08-17	2023-08-17		211	1
W-111V-NWT-HX2-001	C01	P01	SRE	DD	Scheduled	2023-08-17	2023-08-17		211	1
W-155V-DRN-FMW-001	C01	P01	SRE	DD	Scheduled	2023-08-25	2023-08-25		205	5
W-104V-UTL-HX2-001	C01	P01	SRE	DD	Scheduled	2023-09-05	2023-09-05		199	9
W-145-GE0-JQW-002	C01	P01	CIO	F	Scheduled	2023-09-11	2023-09-11		195	5
W-105V -TVT-HX2-001	C01	P01	DH	DD	Scheduled	2023-09-25	2023-09-25		185	5
W-127N-GEO-VEW-001	C01	P01	DH	CD	Scheduled	2023-10-19	2023-10-19		169	9
W-152V-LND-NX1-001	C01	P01	DH	DD	Scheduled	2023-10-20	2023-10-20		168	8
W-154V-DRN-HX2-001	C01	P01	SRE	DD	Scheduled	2023-10-24	2023-10-24		166	6
W-104N-UTL-HY2-001	C01	P01	SRE	CD	Scheduled	2023-10-25	2023-10-25		165	5
W-142N-NWT-GJW-001	C01	P01	SRE	CD	Internal+Consultant	2023-10-24	2023-10-24	2024-06-17	163	3
W_110V_VR I_HV2_001	CN1	DN1	CDE	חח	Schadulad	2022-11-07	2022_11_04		157	7

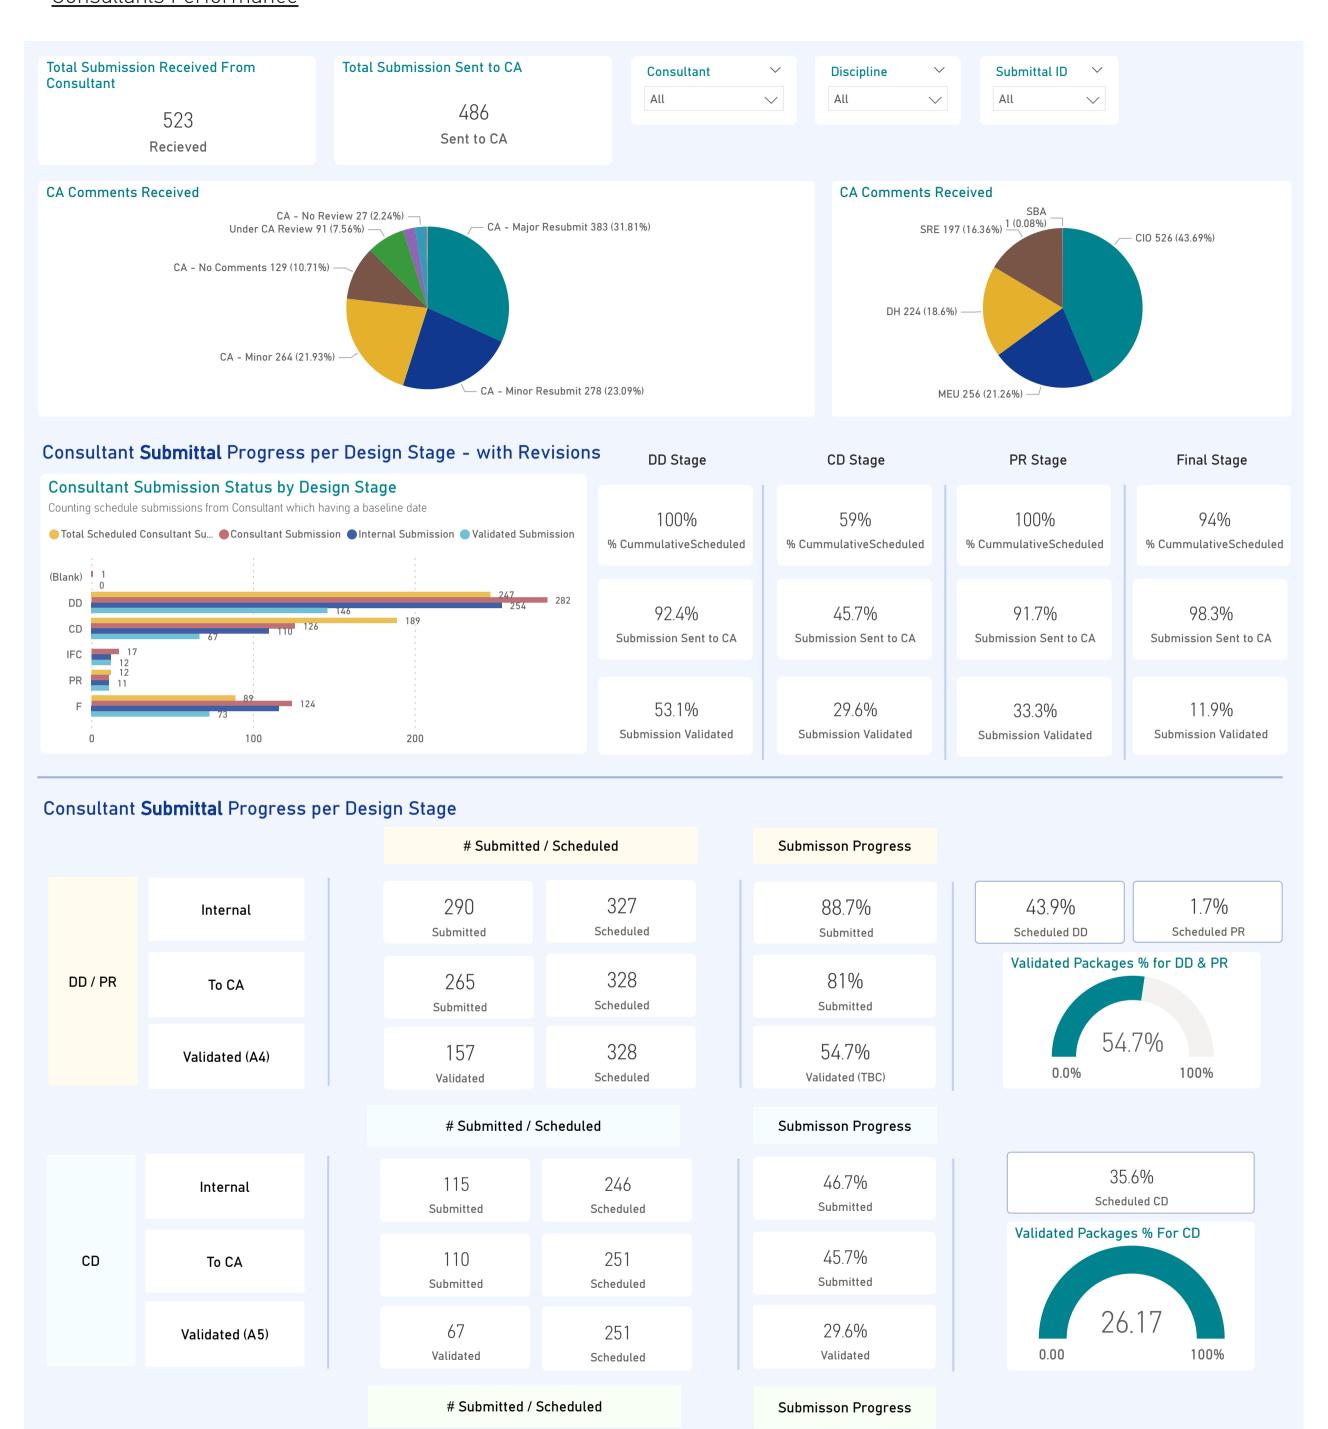




### 2024-06-03 11:34 AM Last Refresh Time

# Consultant Historical Delay Report



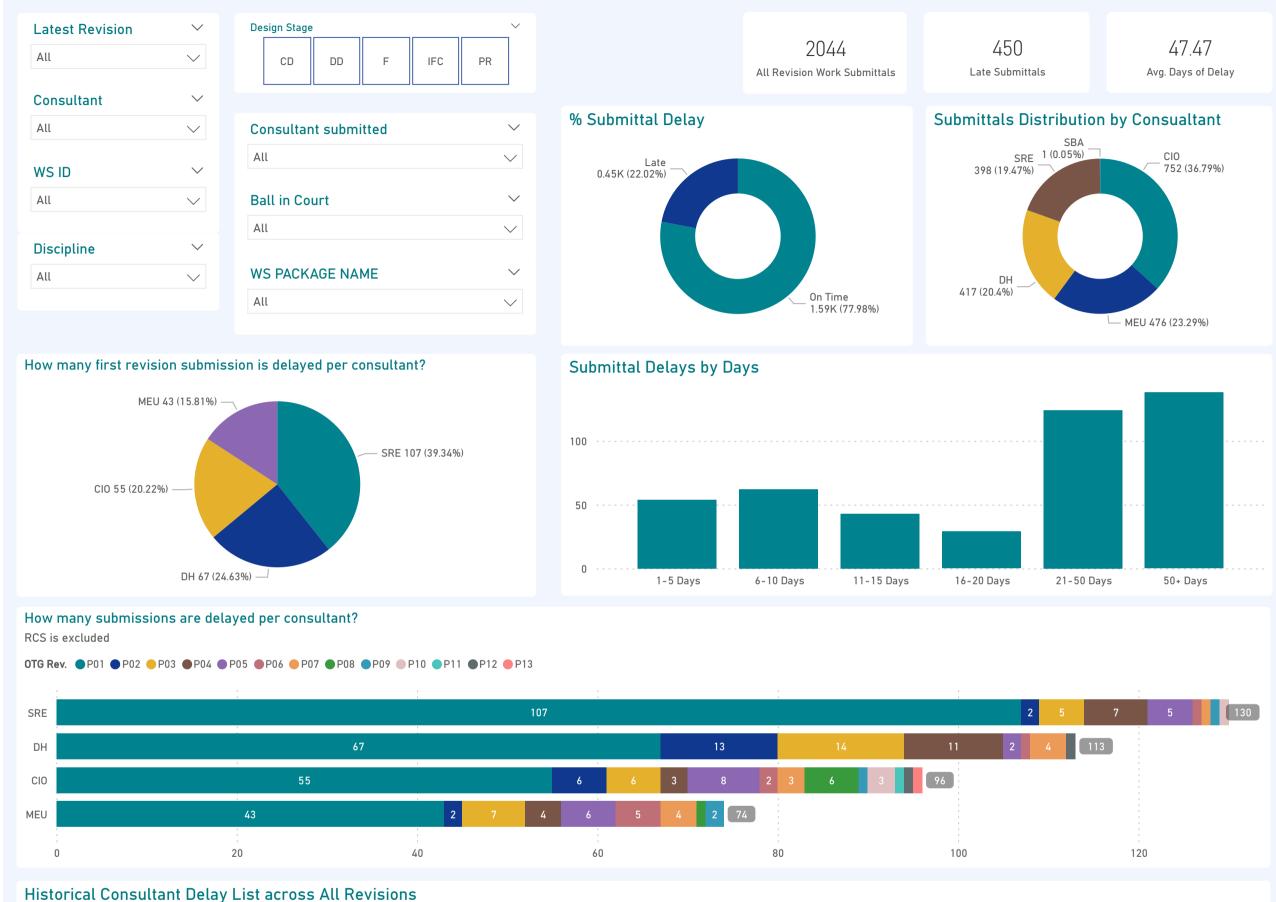

Showing all consultant delayed package including all revisions. RCS is excluded.

WS PACKAGE NAME	CA Rev.	Internal Rev.	Consultant	Design Stage	Ball in Court	Ball in court (simplified)	Consultant Revision Submission Due	Consultant Baseline	Consultant Submission	Consultant Submission Delay in Days ▼
V-201V-TUN-VEW-001	C01	P01	DH	DD	GHD	Scheduled	2023-03-24	2023-03-24		311
JOT-146V-UTL-GJW-001	C01	P01	SRE	DD	R. Closed	Scheduled	2023-06-06	2023-06-06		261
W-242V-HER-NKW-002	C01	P01	CIO	DD	S. Validated	Validated	2023-06-16	2023-06-16		253
P-202J-ELE-PWD-0012	C02	P03	CIO	F	R. Closed	Scheduled	2023-07-28			224
W-104V-UTL-HY2-001	C01	P01	SRE	DD	SENER	Scheduled	2023-07-31	2023-07-31		223
W-139V-FLW-HX2-001	C01	P01	SRE	DD	SENER	Scheduled	2023-08-15	2023-08-15		213
W-111N-NWT-HX2-001	C01	P01	SRE	CD	SENER	Scheduled	2023-08-17	2023-08-17		211
W-111V-NWT-HX2-001	C01	P01	SRE	DD	SENER	Scheduled	2023-08-17	2023-08-17		211
W-155V-DRN-FMW-001	C01	P01	SRE	DD	SENER	Scheduled	2023-08-25	2023-08-25		205
P-202J-ELE-PWD-0012	C02	P04	CIO	F	R. Closed	Scheduled	2023-08-30			202
P-202N-ELE-FMW-001	C02	P03	SRE	F	R. Closed	Scheduled	2023-08-30			202
P-202N-ELE-GJW-001	C02	P03	SRE	F	R. Closed	Scheduled	2023-08-30			202
P-202N-ELE-PWD-0013	C02	P02	CIO	F	R. Closed	Scheduled	2023-08-30			202
W-242V-HER-NKW-001	C02	P02	CIO	DD	S. Validated	Validated	2023-08-31			201

#### TECHNICAL DEPT


# <u>Design Monitoring Tracker Register</u>






2024-06-03 11:34 AM

Last Refresh Time



WS ID	WS PACKAGE NAME	CA Rev.	Internal Rev.	Latest Rev	Location	Discipline	ORIGINATOR	Description	Ball in Court	Design Stage	Revision S (Doc.Con
W-128J	W-128J-GEO-GJW-001	C03	P05	Υ	GJW	GE0	SRE	CINR Level 2   Level 3 - C1	Internal	F	Under Interi Review
WPR-000	WPR-000-PRM-D0W-001	C01	P01	Υ	DOW	PRM	MEU	COT-RPR-100 to RPR-133 Rite Plan Reviews Package - L1	CA	DD	Under CA Ro
V-201N	V-201N-TUN-DOW-001- 02	C03	RCS- P04	Y	DOW	TUN	MEU	N-201 - RoE - CD - L1 Rtation - Routh Rhaft (RCR Only)	Internal	CD	Under Interi Review
V-201N	V-201N-TUN-DOW-001- 03	C01	P04	Υ	DOW	TUN	MEU	N-201 - RoE - CD - L1 Rtation - University Nvenue Vent Rhaft	Internal	CD	Under Interi Review
V-201N	V-201N-TUN-GJW-001	C05	P13	Υ	GJW	TUN	SRE	RoE   CD - C1	CA	CD	Under CA Ro
W-111N	W-111N-NWT-NKW-002- 02	C01	P02	Υ	NKW	NWT	CIO	KK - Routh Rhaft - Rtructural Design - CD	Internal	CD	Under Interi Review
W-127V	W-127V-GEO-NKW-001	C05	P09	Υ	NKW	GE0	CIO	R-127- GIMP Design Report- DD- KK	Internal	DD	Under Interi Review
W-127V	W-127V-GEO-NV1-001	C02	P04	Υ	NV1	GE0	DH	R-127N - GIMP Report - Rtrachan CRO and Critical Utilities-T	Internal	DD	Under Interi Review
W-137N	W-137N-FLW-FMW-001	C01	P01	Υ	FMW	FLW	SRE	R-137B - FLR Report - CD - M21	Internal	CD	Under Interi Review
W-138N	W-138N-FLW-FMW-001	C01	P01	Υ	FMW	FLW	SRE	R-138B - FLR Design - CD - M21	Internal	CD	Under Interi Review
W-155V	W-155V-NWT-EQW-001	C01	P01	Υ	EQW	NWT	MEU	R-155N - B Hudson Bay Package	Internal	DD	Under Interi





# PMT Packages

